



HELIDECK INFORMATION PLATE

NUI**Ravenspurn North ST2****EGZV****GENERAL INFORMATION:**

OPERATOR	HLAC ISSUE DATE	HLAC EXPIRY DATE	
Perenco UK Ltd	13 Dec 2024	23 Jul 2026	
HELIDECK ELEVATION	VAR	POSITION	
123ft	Check	N54 03.2 E001 02.00	
INSTALATION HEIGHT	HIGHEST OBSTACLE	D VALUE	
123ft	Within 5nm:	UK: 15m	NOR Dh:N/Am (1.25D)
T VALUE	TD/PM & H LIGHTING	PITCH / ROLL / HEAVE CATEGORY	
5.3t	Yes	0	

COMMUNICATIONS:

VHF FREQUENCIES		NDB	
Traffic: 129.880	Logistics: Check	N/AKhz	Ident: N/A

TURNAROUND:

FUELING INSTALATION	STARTING EQUIPMENT
No	No

LIMITATION & NON-COMPLIANCES:

LIMITATIONS / COMMENTS	WIND DIRECTION (T°)	WIND SPEED (Kts)
Daylight operations only - Circle & "H" lights isolated		
Table 1 (T) if overflight of 5:1 items unavoidable		
CAP437 Appendix H Risk Assessment required for AW139 operations		

NON-COMPLIANCES - 210°

Sub 16m deck. Items in excess of 50mm adl:
Perimeter lights 130mm
Speakers 210mm
Cable junction boxes north/south side 110mm
Handrails + hinges 130mm adl (when folded).

NON-COMPLIANCES - 150°

Nil

NON-COMPLIANCES - 5:1

South & North access platform + crane jib when in rest.

NON-COMPLIANCES - Miscellaneous

Gull Scat fitted (Bird scaring system - irregular loud noises)
No automatic fire-fighting facilities.

IMAGE LIBRARY:

LOOKING NORTH (T)



LOOKING EAST (T)




LOOKING SOUTH (T)



LOOKING WEST (T)



PLAN DRAWING

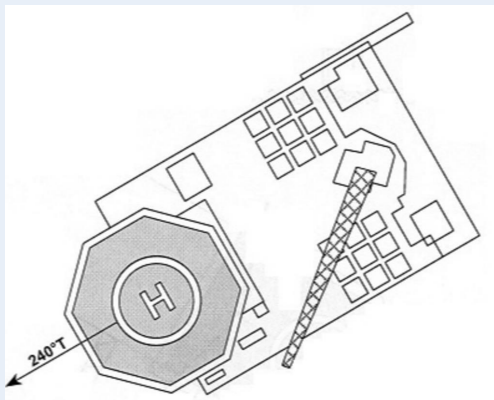

ADDITIONAL (IF AVAILABLE)

