



HELIDECK INFORMATION PLATE

Jack Up

Voltaire

XVOT

GENERAL INFORMATION:

OPERATOR	HLAC ISSUE DATE	HLAC EXPIRY DATE	
Jan De Nul Group NV-European Dredging Company SA	25 Jan 2025	25 Apr 2025	
HELIDECK ELEVATION	VAR	POSITION	
0ft	Mobile	Mobile	
INSTALATION HEIGHT	HIGHEST OBSTACLE	D VALUE	
0ft	Within 5nm: Check	UK: 22.8m	NOR Dh:18.24/SLA = 22.8mm (1.25D)
T VALUE	TD/PM & H LIGHTING	PITCH / ROLL / HEAVE CATEGORY	
14.6t	Yes	1	

COMMUNICATIONS:

VHF FREQUENCIES		NDB	
Traffic: Check	Logistics: Check	N/AKhz	Ident: N/A

TURNAROUND:

FUELING INSTALATION	STARTING EQUIPMENT
No	Yes

LIMITATION & NON-COMPLIANCES:

LIMITATIONS / COMMENTS	WIND DIRECTION (T°)	WIND SPEED (Kts)
Jack-Up ship - helideck on bow offset to starboard		
Table 1(T&L) if overflight of 5:1 items is unavoidable		
Crane MUST be aft of forward legs for all helicopter operations		
HMS rev.9B + Lights fitted		

NON-COMPLIANCES - 210°

Nil

NON-COMPLIANCES - 150°

Nil

NON-COMPLIANCES - 5:1

Starboard access platforms is a marginal infringement approx 3.1m from edge helideck

NON-COMPLIANCES - Miscellaneous

Nil

IMAGE LIBRARY:


STARBOARD SIDE



PORT SIDE



PLAN DRAWING

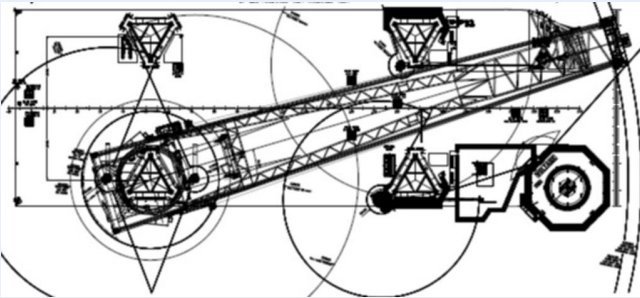

ADDITIONAL (IF AVAILABLE)

